


Sprint 2 Burndown Chart

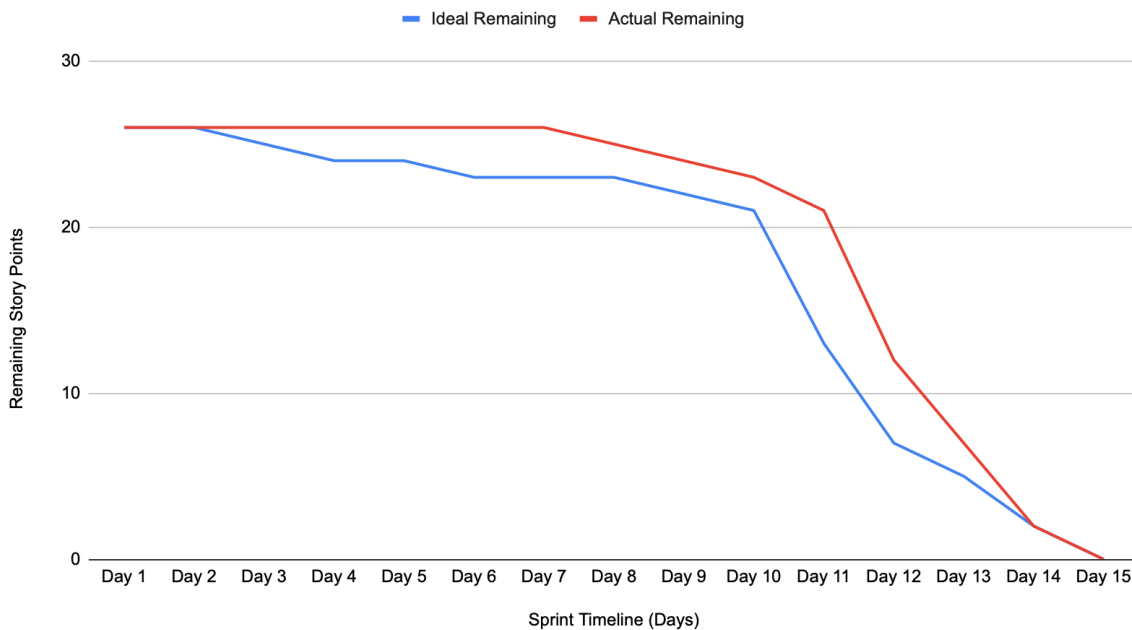

Burndown Chart

The burndown chart shows Sprint 2 progress from March 9 to March 23 using the Trello user stories and their story point values. The sprint started with 26 story points. The ideal line was planned to stay a bit flatter at the beginning of the sprint, since the early phase focused more on breaking user stories into smaller subtasks and starting implementation. The actual line also stayed flat at the start, which shows that while work was progressing through those subtasks, full user stories had not yet been completed. In the second half of the sprint, the actual line dropped faster than the ideal line, as several stories were fully finished, tested, reviewed, and moved to completed in Trello. Overall, the actual progress followed the expected pattern of a slower start and a heavier completion period later in the sprint.

Velocity Comparison

The planned velocity for Sprint 2 was 26 story points, while the previous sprint velocity from Sprint 1 was 16 story points. The velocity increased from Sprint 1 to Sprint 2 because Sprint 2 had more work and more depth within the user stories. Many stories were broken into multiple subtasks, so more implementation, testing, and review were needed before the full story could be marked complete. This made the sprint workload larger than Sprint 1, which is why the planned velocity was higher.
